

City Manager's Report

Presented by Mario Juarez-Infante, PE, City Manager
07.21.2026



Summary



- Calle Carrousel and Obregon Construction Project Schedule
- Rio Grande Trail Phase II *Construction Update*
- City Leaders, City Directors, and Members from GISD Site Tour


Calle Carrousel and Obregon *Construction Project Schedule*



Project Schedule



Calle Carrousel & Obregon Improvements Sunland Park, New Mexico

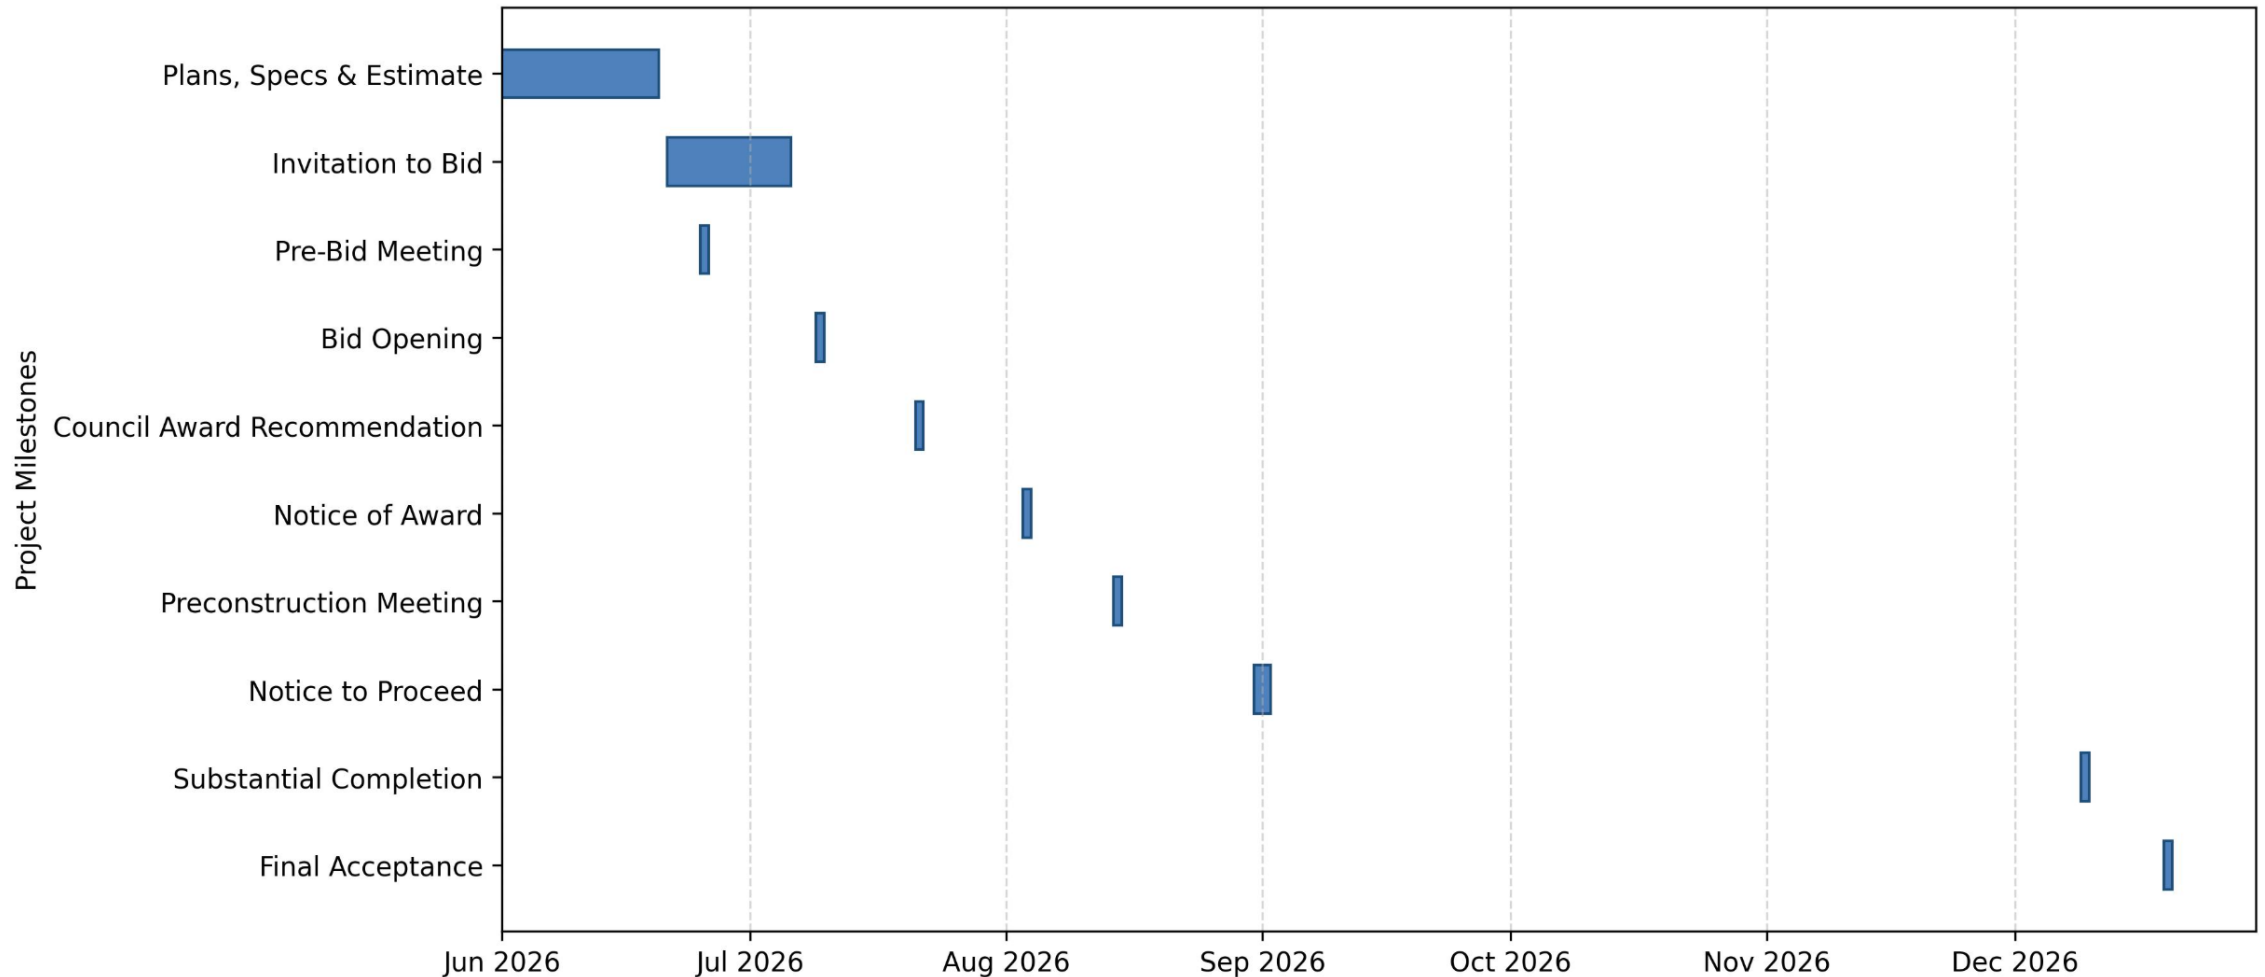

Rio Grande Trail Phase II *Construction Update*



- Construction Contract Price: \$1,187,693.59 including NMGR (excludes Material Testing and Construction Management)

- Aggregate base course installation completed
- 10-ft wide trail form placement in process with concrete pours to start week of 7.27, pending rains
- Sub-stantial completion is October 13, 2026
- Final completion is October 30, 2026



City Leaders, City Directors, and Members from GISD Site Tour



Site Tour

- When: Thursday, July 23, 2026, from 11:00 a.m. to ~1:00 p.m.
- Where: Capital Projects throughout the City
- Why: Learn about sustainable eco-friendly projects that address long-term water conservation, aquifer recharge, and sediment capture and removal before reaching the Rio

WE ARE THE GATEWAY TO THE LAND OF ENCHANTMENT

SITE TOUR AGENDA

CITY COUNCIL PRESENTATION



ARRIVE
10:50 a.m.



DEPART
11:00 a.m.



**COLLABORATE
EXPLORE
BUILD**

*Working together for
a stronger community.*

1



Arrive at 10:50 a.m.

2



Depart at 11:00 a.m.

3



Sites

- a Carlos Aguirre Flood Control
- b Understanding the bi-national combined sewer overflow
- c Rio Grande Trail
- d Guitar Social Complex
- e South Lift Station Access Road
 - i Linear flood control Passive Park
 - ii Sediment & Urban Conservation Park
- f Multi-generational Center

4



Lunch & Presentation



SAFE



CONNECTED



SUSTAINABLE



PROGRESSIVE

Building a Better Sunland Park



SUNLAND PARK



Questions?
